




# 'L' System Slow Zone Map

July 31, 2017

## Notes

Overall system slow zones in July 2017 were 8.2% for the month, an increase from the previous month. CTA removed slow zones near the Pulaski and Western stations on the Forest Park branch of the Blue Line, and between the Francisco and Kedzie Brown Line stations. Slow zones were added near the Clinton and King Drive Green Line stations, the Addison Red Line and between the Central and Foster Purple Line stations due to track conditions. Slow zones were also added along the O'Hare branch of the Blue Line due to third rail replacement work, and in the Red Line's State Street Subway due to ongoing track maintenance and subway tunnel cleaning.

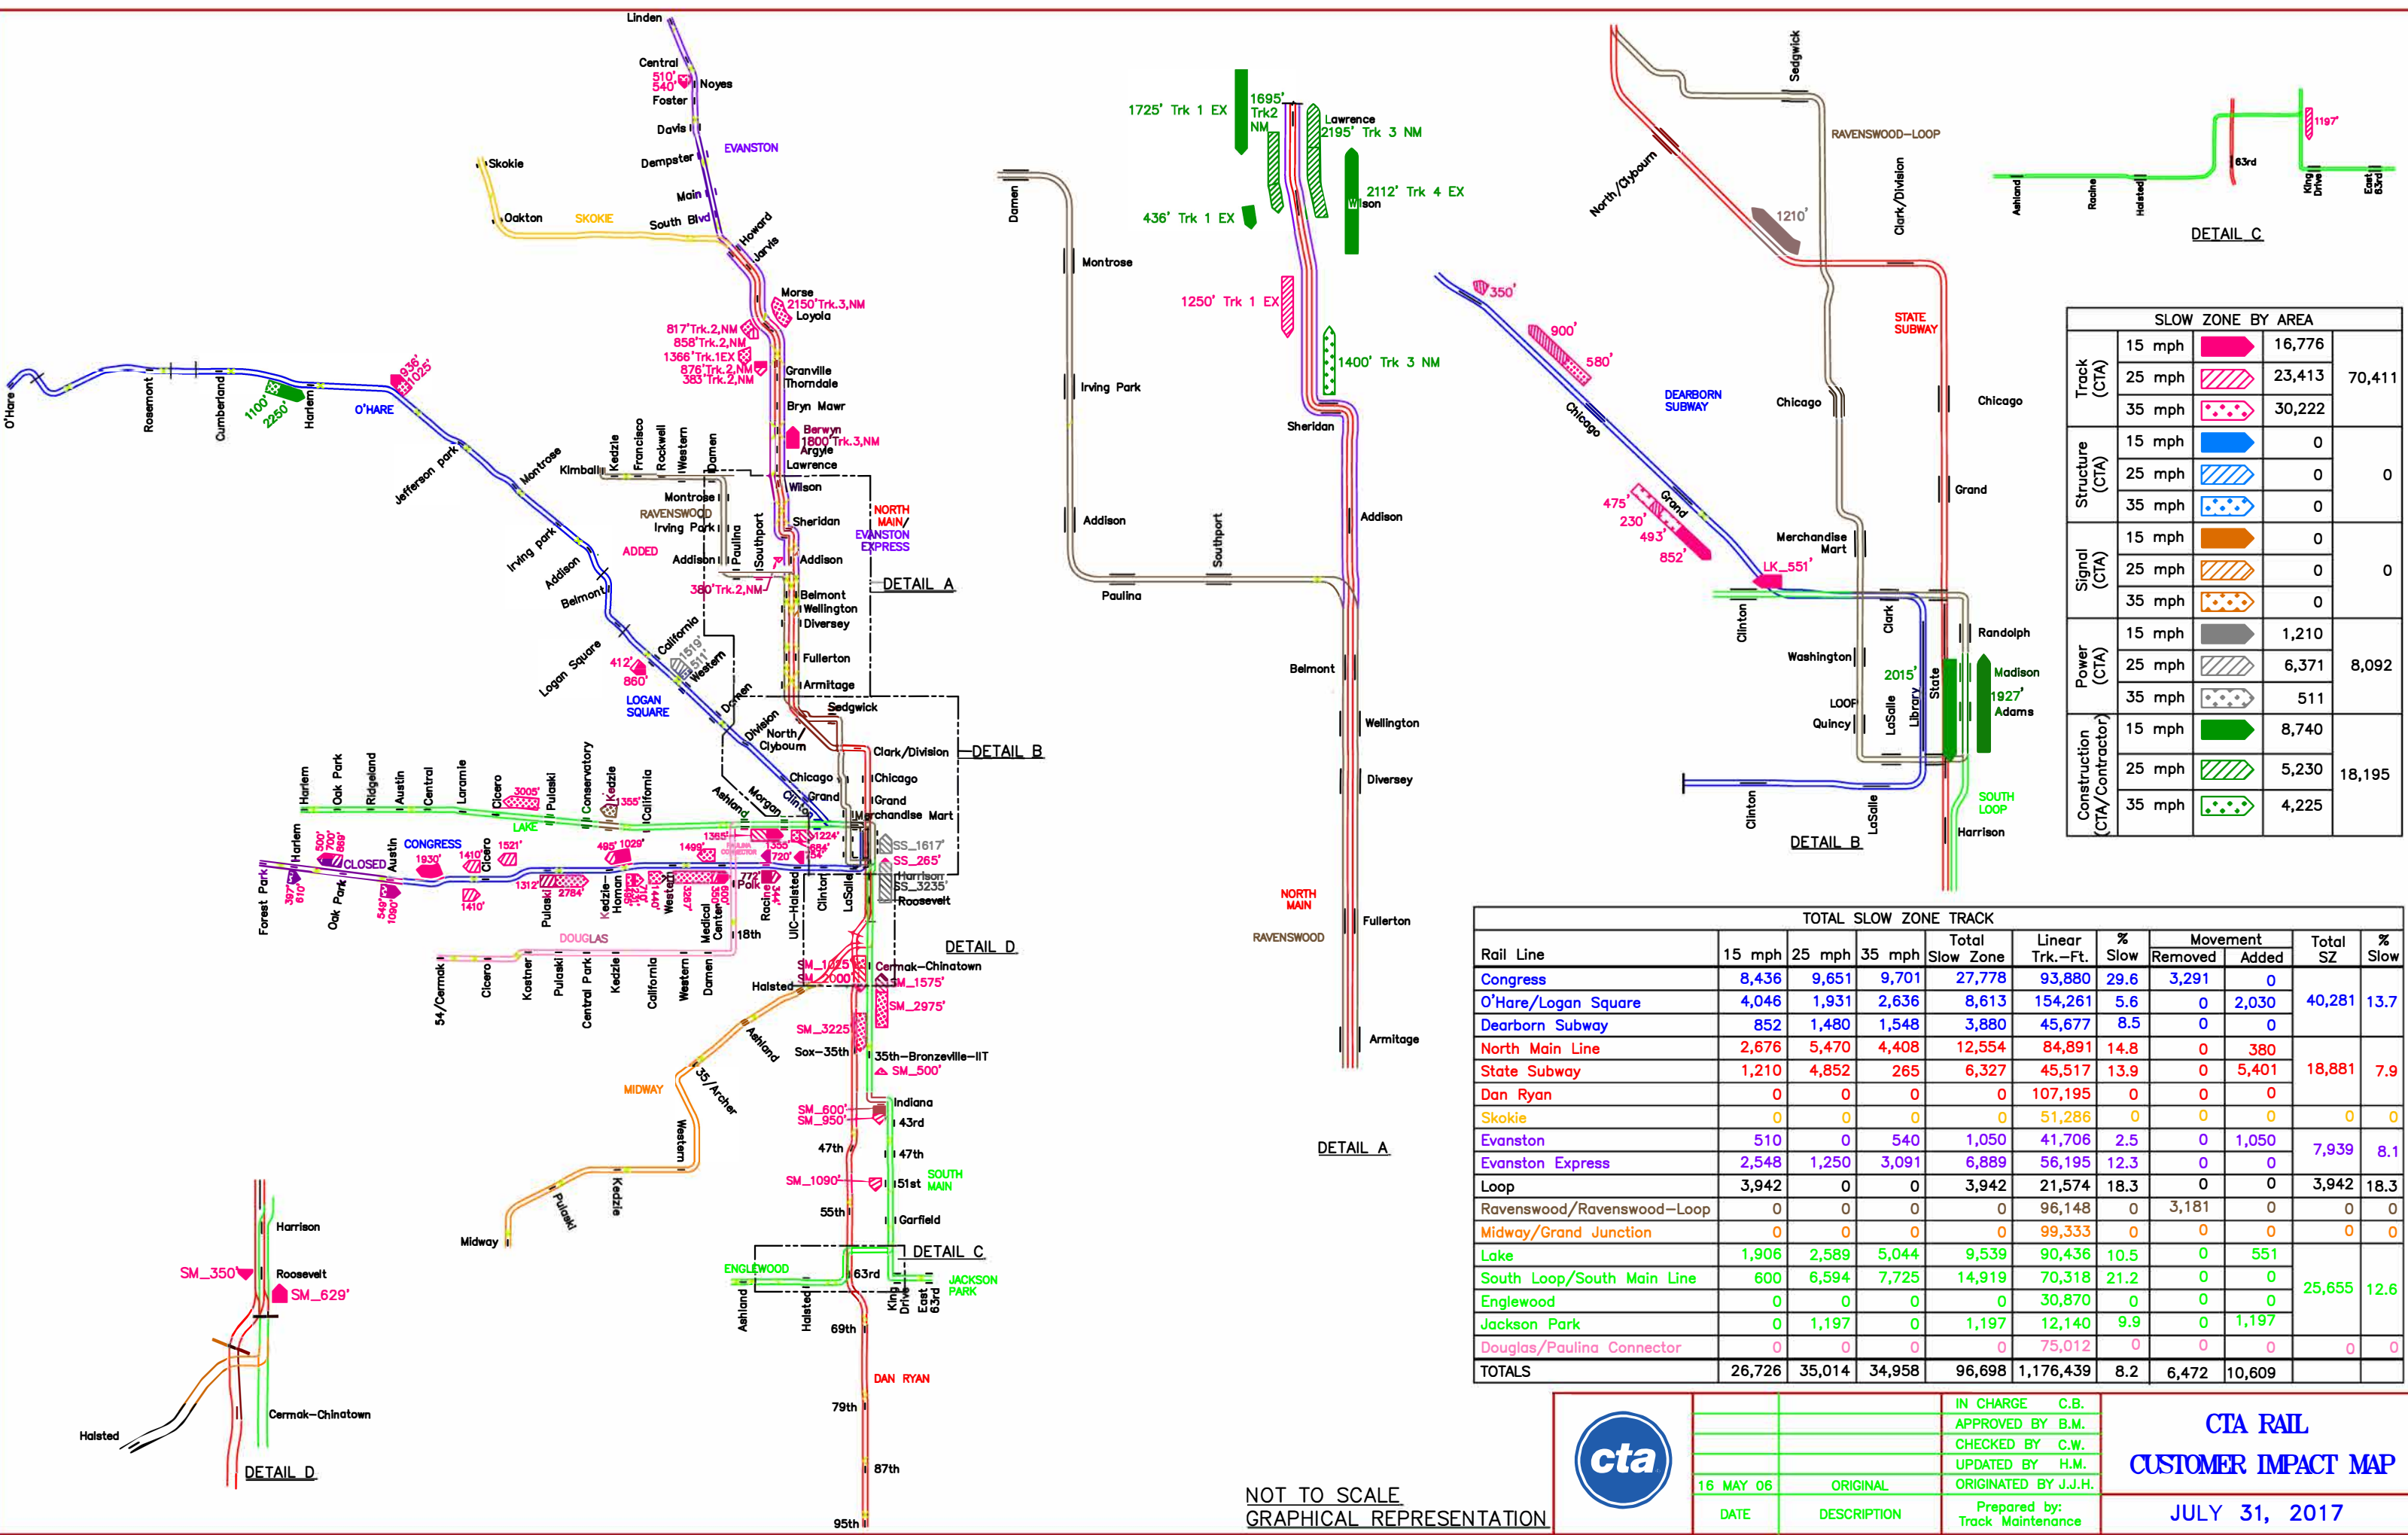

SLOW ZONE BY AREA				
Track (CTA)	15 mph		16,776	70,411
	25 mph		23,413	
	35 mph		30,222	
Structure (CTA)	15 mph		0	0
	25 mph		0	
	35 mph		0	
Signal (CTA)	15 mph		0	0
	25 mph		0	
	35 mph		0	
Power (CTA)	15 mph		1,210	8,092
	25 mph		6,371	
	35 mph		511	
Construction (CTA/Contractor)	15 mph		8,740	18,195
	25 mph		5,230	
	35 mph		4,225	

TOTAL SLOW ZONE TRACK										
Rail Line	15 mph	25 mph	35 mph	Total Slow Zone	Linear Trk.-Ft.	% Slow	Movement		Total SZ	% Slow
							Removed	Added		
Congress	8,436	9,651	9,701	27,778	93,880	29.6	3,291	0	40,281	13.7
O'Hare/Logan Square	4,046	1,931	2,636	8,613	154,261	5.6	0	2,030		
Dearborn Subway	852	1,480	1,548	3,880	45,677	8.5	0	0		
North Main Line	2,676	5,470	4,408	12,554	84,891	14.8	0	380	18,881	7.9
State Subway	1,210	4,852	265	6,327	45,517	13.9	0	5,401		
Dan Ryan	0	0	0	0	107,195	0	0	0		
Skokie	0	0	0	0	51,286	0	0	0	0	0
Evanston	510	0	540	1,050	41,706	2.5	0	1,050	7,939	8.1
Evanston Express	2,548	1,250	3,091	6,889	56,195	12.3	0	0		
Loop	3,942	0	0	3,942	21,574	18.3	0	0	3,942	18.3
Ravenswood/Ravenswood-Loop	0	0	0	0	96,148	0	3,181	0	0	0
Midway/Grand Junction	0	0	0	0	99,333	0	0	0	0	0
Lake	1,906	2,589	5,044	9,539	90,436	10.5	0	551	25,655	12.6
South Loop/South Main Line	600	6,594	7,725	14,919	70,318	21.2	0	0		
Englewood	0	0	0	0	30,870	0	0	0		
Jackson Park	0	1,197	0	1,197	12,140	9.9	0	1,197	0	0
Douglas/Paulina Connector	0	0	0	0	75,012	0	0	0	0	0
<b>TOTALS</b>	<b>26,726</b>	<b>35,014</b>	<b>34,958</b>	<b>96,698</b>	<b>1,176,439</b>	<b>8.2</b>	<b>6,472</b>	<b>10,609</b>		

IN CHARGE C.B.  
 APPROVED BY B.M.  
 CHECKED BY C.W.  
 UPDATED BY H.M.  
 ORIGINATED BY J.J.H.

**CTA RAIL  
 CUSTOMER IMPACT MAP**

16 MAY 06  
DATE

ORIGINAL  
DESCRIPTION

Prepared by:  
Track Maintenance

**JULY 31, 2017**

NOT TO SCALE  
 GRAPHICAL REPRESENTATION
